Minutes of Meeting - Agenda

Portfolio	*DG2-Diriyah Gate Phase 2 – Infrastructure Package 1*			
Project	*DGII-Infrastructure Package 1*			
Title	*Infrastructure Package 1 – Weekly OHS Meeting*			
Date	*20– Oct- 2025*	*Time: 09:00 AM*	*Meeting #: 92*	*Location: AICC New office*

Invite /Attendees

Name	***Organization***	***Designation***
Asma Othman	*DC*	*Construction Safety Assist Manager*
Metaeb Alharbi	*DC*	*Construction Safety Senior Manager*
Rajih	*DC*	*Construction Safety Manager*
Imran S Khan	*Aecom*	*Safety Senior Manager*
Sushel Kurup	*Aecom*	*Safety Manager*
Majed Saleh	*Aecom*	*APM*
Hamzan Alghamdi	*Aecom*	*OHS*
Adel Al Harbi	*Jacobs*	*Sr. Safety Manager*
Ali Nabil	*Jacobs*	*Safety Manager*
Muneer Ali	*Jacobs*	*LO*
Renante	*Jacobs*	*Safety Inspector.*
Rawabi Al Muhanna	*Jacobs*	*Safety Advisor*
Walid Rasheed	*AICC*	*Sr.OHS Manager*
Rameez iftigar	*AICC*	*Safety Admin*
Abdullah Sabry	*AICC*	*CD*

Prepared By:	*Rawabi Al Muhanna – Jacobs*

The following listing comprises the intended agenda for the DGII Infra 01 Project weekly OHS meeting.

Item	***Description***	***Action Owner***	***Planned/Due Date***	***Forecast Date***	***Status***
1.0	***Introduction***				
1.1	*Safety moment on Safety communication: “**Ladder Safety**”*				
2.0	***OHS Weekly KPIs***				
3.0	***Submittals***				
4.0	***CVs & OHS Personnel Approval***				
5.0	***Emergency Management***				
6.0	**Mobilization**				

7.0	***OHS Observations / Concerns***				
7.1	*PMC highlighted to increase the mess-hall facilities to accommodate the current workforce and ensure sufficient capacity.* *-PMC is in coordination with SWL with expected completion is 30 Sept 25* ***-SWL rejected the LAAR proposal; AICC to revise and resubmit for approval.*** ***- AICC resubmitted – No approval yet from SWL for the proposal.*** ***Action Ongoing -Approval from SWL is expected this week.*** ***AICC instructed to inspect all tent.***	*AICC/PMC*	~~07-July-2025~~ 20-Oct-2025		*Open*
7.2	*CSC instructed AICC to submit the list of approved subcontractors for CSC records.* *Action ongoing – DC has instructed to improve communication and ensure timely closure.* *AICC to officially submit the list of subcontractor approval to CSC H&S as evidence.* *AICC confirmed to submit the approved list by COB.* ***The subcontractor's list has not been received.*** ***DC advised the AICC to provide AICC vests to all subcontractor workers.***	*AICC*	~~01-Sept -2025~~ 20-Oct-2025		*Open*
7.3	*DC instructed AICC to update the* ***health surveillance records in the PMIS*** *ensuring records maintained are up to date. (160 workers- Pending)* *AICC stated that updates ongoing and will be completed maximum by this week.* *Action Ongoing- AICC confirmed to update the remaining by COB.* ***Action Ongoing***	*AICC*	~~01-Sept -2025~~ 20-Oct-2025		*Open*
7.4	*CSC instructed AICC management intervention on the repeated scaffold and unsafe work at height practices involving use of ladders in the MV Culvert.* *No improvements on the site- DC has instructed to conduct a workshop and to assign a competent engineer to inspect and verify all scaffolding and formwork and document all associated risk and assessments.* *AICC committed to submit a comprehensive action plan based on the outcomes and agreements finalized during the scaffold safety workshop by COB.* *AICC to assign a focal person for work-at-height activities and develop a compliance checklist.* ***The action is currently ongoing. The scaffolding register, TPC, and inspection checklist are still pending.*** ***As confirmed by AICC, the remaining items are expected to be completed by October 23, 2025.***	*AICC*	~~15 Sept 2025~~ 20-Oct-2025		*Open*
7.5	*DC advised AICC to develop a separate safe work plan taking into consideration of current and upcoming activities including confined space works in the MV Culvert.* *AICC confirmed coordination with construction is underway to develop the safe work plan* *Action Ongoing- AICC committed to share the action plan by COB.* ***Action item is pending.***	*AICC*	~~22 Sept 2022~~ 20-Oct-2025		*Open*
7.6	*PMC directed AICC to conduct incident and near miss reporting to ensure awareness and compliance.* ***Action is pending*** ***The AICC was advised to include managers, engineers, and supervisors in the awareness session and to share the invitation with all relevant stakeholders.***	*AICC*	06 Oct 2025 20-Oct 2025		*Open*
7.7	*CSC instructed AICC to revise and resubmit Code-B MSRAs for Code-A approval, ensuring monthly contractor compliance evaluations (KPI scores) are not impacted.* ***Action is pending***	*AICC*	13 Oct 2025 20-Oct-2025		*Open*
7.8	*CSC instructed AICC to conduct MSRA briefings for the workforce and maintain evidence of records.* ***AICC CD confirms that this action will commence on October 21, 2025.***	*AICC*	13 Oct 2025 20-Oct-2025		*Open*
7.9	*It was noted that AICC Construction team consistently delayed participation in safety walks.* *Attendance sheet with participants name will be shared to ensure attendance.*	*AICC*	13 Oct 2025 20-Oct-2025		*Open*

8.0	*AICC was instructed to submit flood mitigation plan for CSC review.* ***Under CSC review****.*	*AICC*	13 Oct 2025 20-Oct-2025		*Open*
8.1	*AICC was instructed to prepare action plan for focused inspection conducted on the generators.* ***CSC still did not receive the close out from AICC.***	*AICC*	13 Oct 2025 20-Oct-2025		*Open*
8.2	*CSC noted delays in SOR close-out submissions from AICC and instructed timely submission moving forward.* ***Action Ongoing***	*AICC*	13 Oct 2025 20-Oct-2025		*Open*
8.3	*DC has instructed to assign a dedicated and comprehensive housekeeping team, effective from next Sunday.*	*AICC*	20-Oct-2025		*Open*
8.0	***AOB***				
Next Meeting	***Date***	***Time***			
	27-Oct-2025	*9:00 AM*			

شركة الدرعية
Diriyah Company

OH&S Weekly Meeting #92

Cut off – 16th October 2025;

DD-2022- **DGII- Infrastructure Package 1**

AECOM Jacobs العيوني AL-AYUNI

Agenda

1. Safety Moment
2. Previous Meeting Minutes
3. OH&S Weekly KPIs (Leading and Lagging Indicators)
4. OH&S Achievements, Reward and Recognition,
5. Good Observation, Positive Engagement, etc.
6. OH&S Incident/s Brief
7. OH&S Submittals Status (Plans, MSRA, Reports and HSE Staff/ Resources)
8. Site SORs and NCR Status
9. Critical Open SORs and NCRs
10. Weekly OHS Activities
11. Critical Escalated OH&S Issues
12. Next Week Look Ahead

Safety Moment – 🪜 Ladder Safety

🪜 Safety Moment: Ladder Safety

Description:
Ladders are one of the most used tools on construction and maintenance sites, but improper use often leads to serious injuries such as falls, fractures, or head trauma. Most ladder-related incidents occur due to unstable placement, overreaching, damaged ladders, or failure to maintain three points of contact. Safe ladder use requires proper inspection, positioning, and user awareness.

Key Safety Measures:

- Always **inspect ladders** before use — check for cracks, loose rungs, and stability.
- Place the ladder on a **firm, level surface** and secure it to prevent slipping.
- Maintain **three points of contact** (two hands and one foot, or two feet and one hand) always.
- **Do not overreach** — keep your belt buckle between the ladder rails.
- Ensure the ladder **extends at least 1 meter (3 feet)** above the landing point.
- **Do not overload** the ladder — follow the manufacturer’s weight limit.
- Keep the **area around the base** of the ladder clear of tools and debris.
- Avoid using ladders in **strong wind or rain and** never move a ladder while someone is on it.

Safety Message:

“Always climb with care — one step of caution can prevent a fall.”

🪜 Safety Moment: Ladder Safety

16 Oct 2025 at 8:21:21 AM
Ad Dir'iyah
العيوني
AL-AYUNI

Previous Minutes

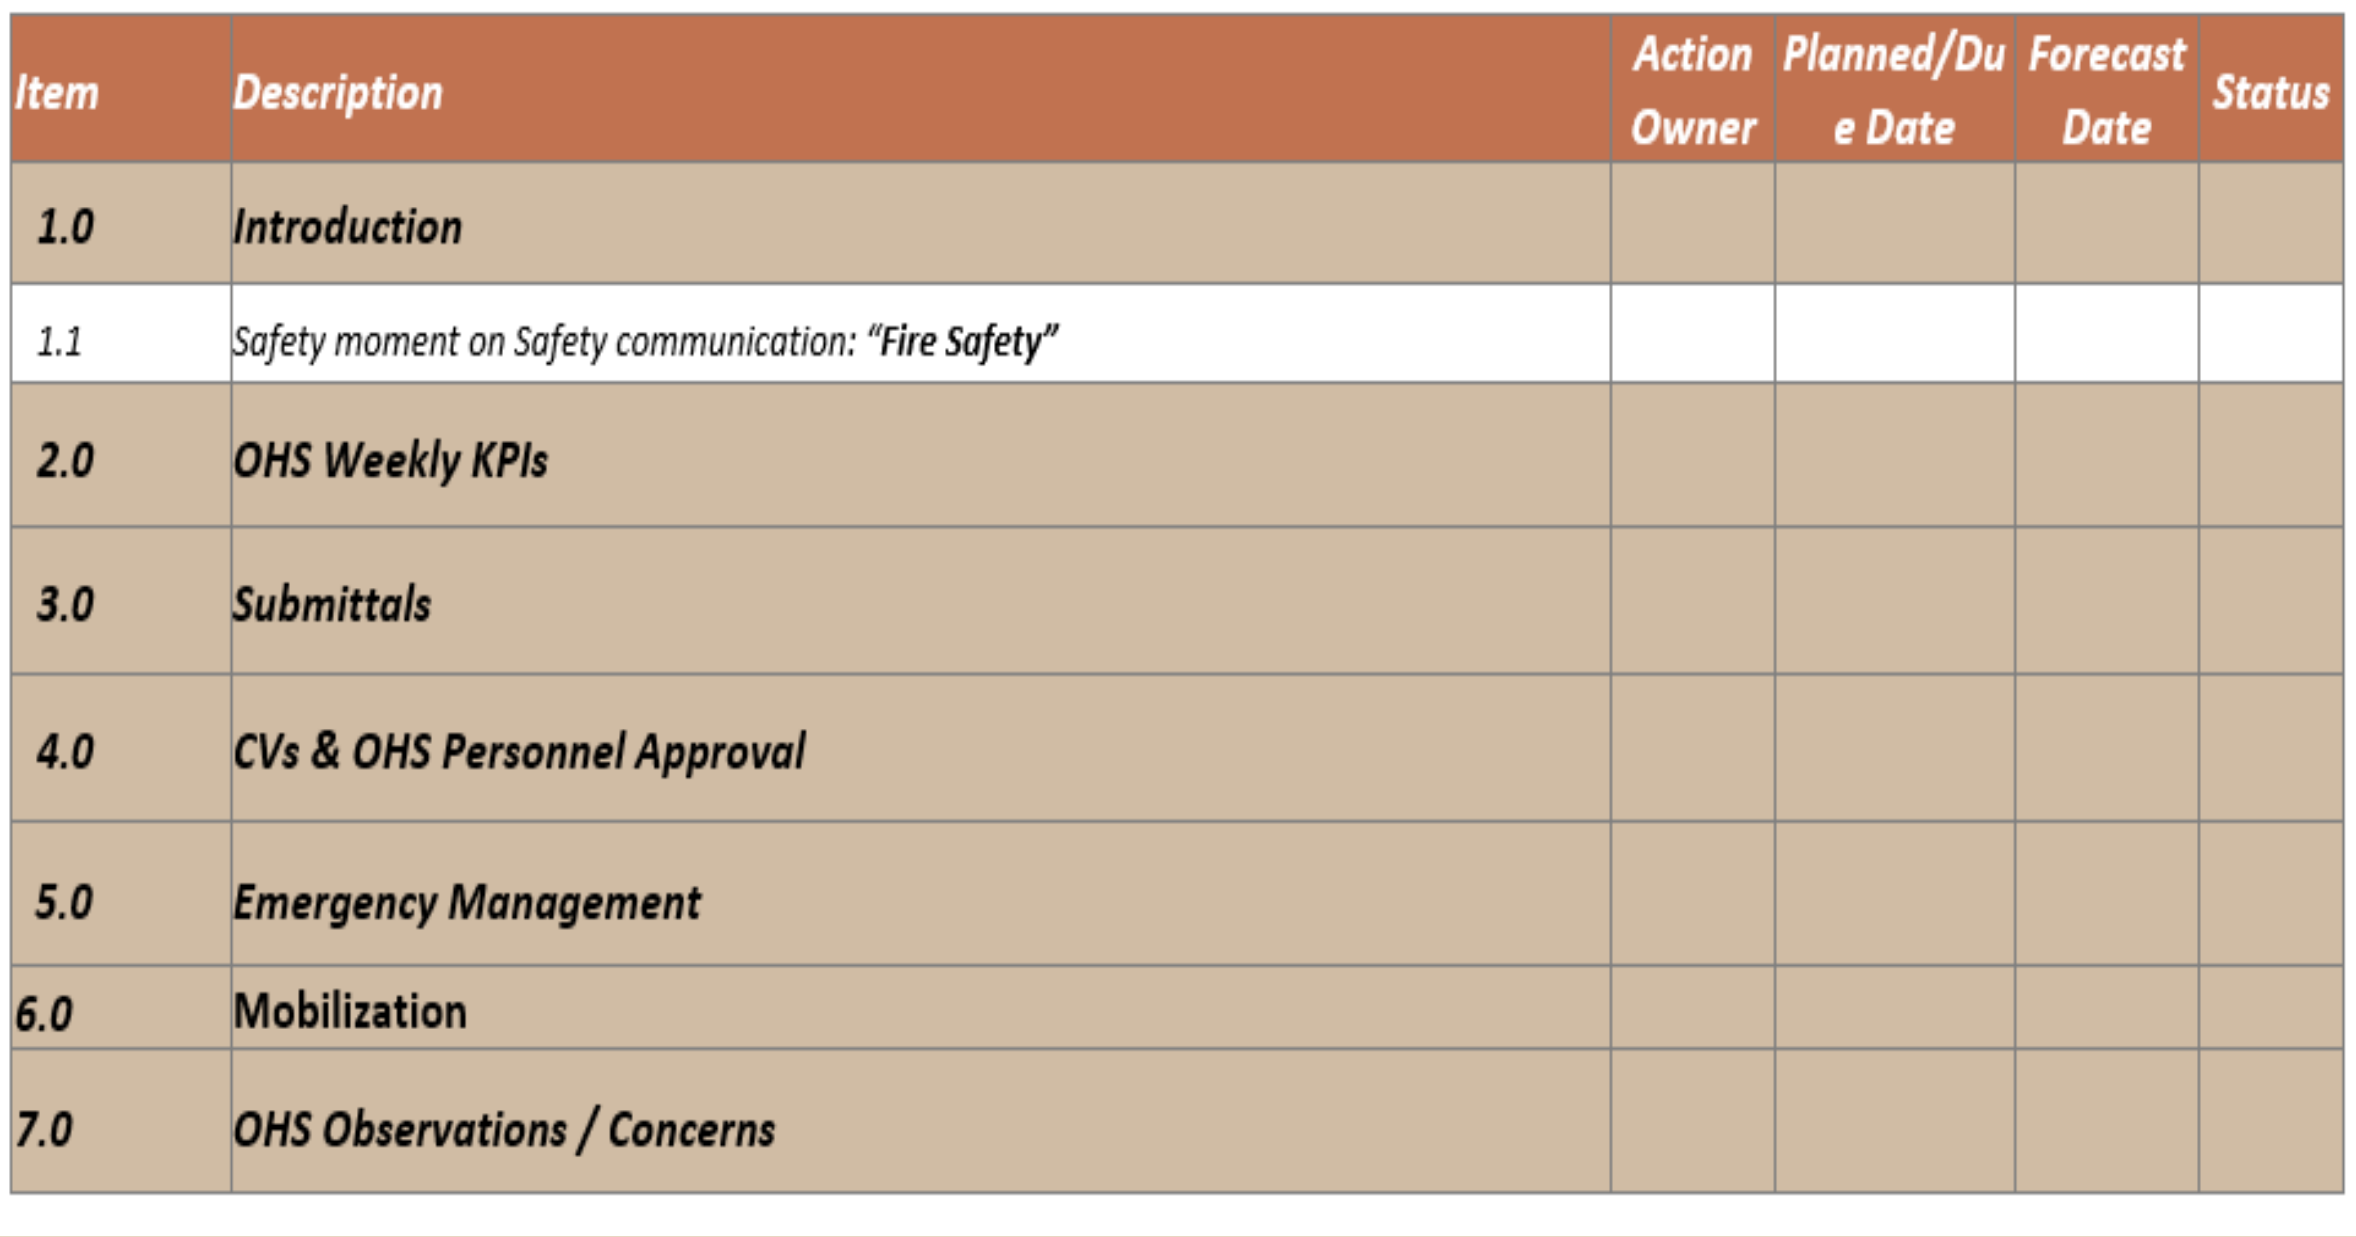

Item	Description	Action Owner	Planned/Due Date	Forecast Date	Status
1.0	**Introduction**				
1.1	Safety moment on Safety communication: **"Fire Safety"**				
2.0	**OHS Weekly KPIs**				
3.0	**Submittals**				
4.0	**CVs & OHS Personnel Approval**				
5.0	**Emergency Management**				
6.0	**Mobilization**				
7.0	**OHS Observations / Concerns**				

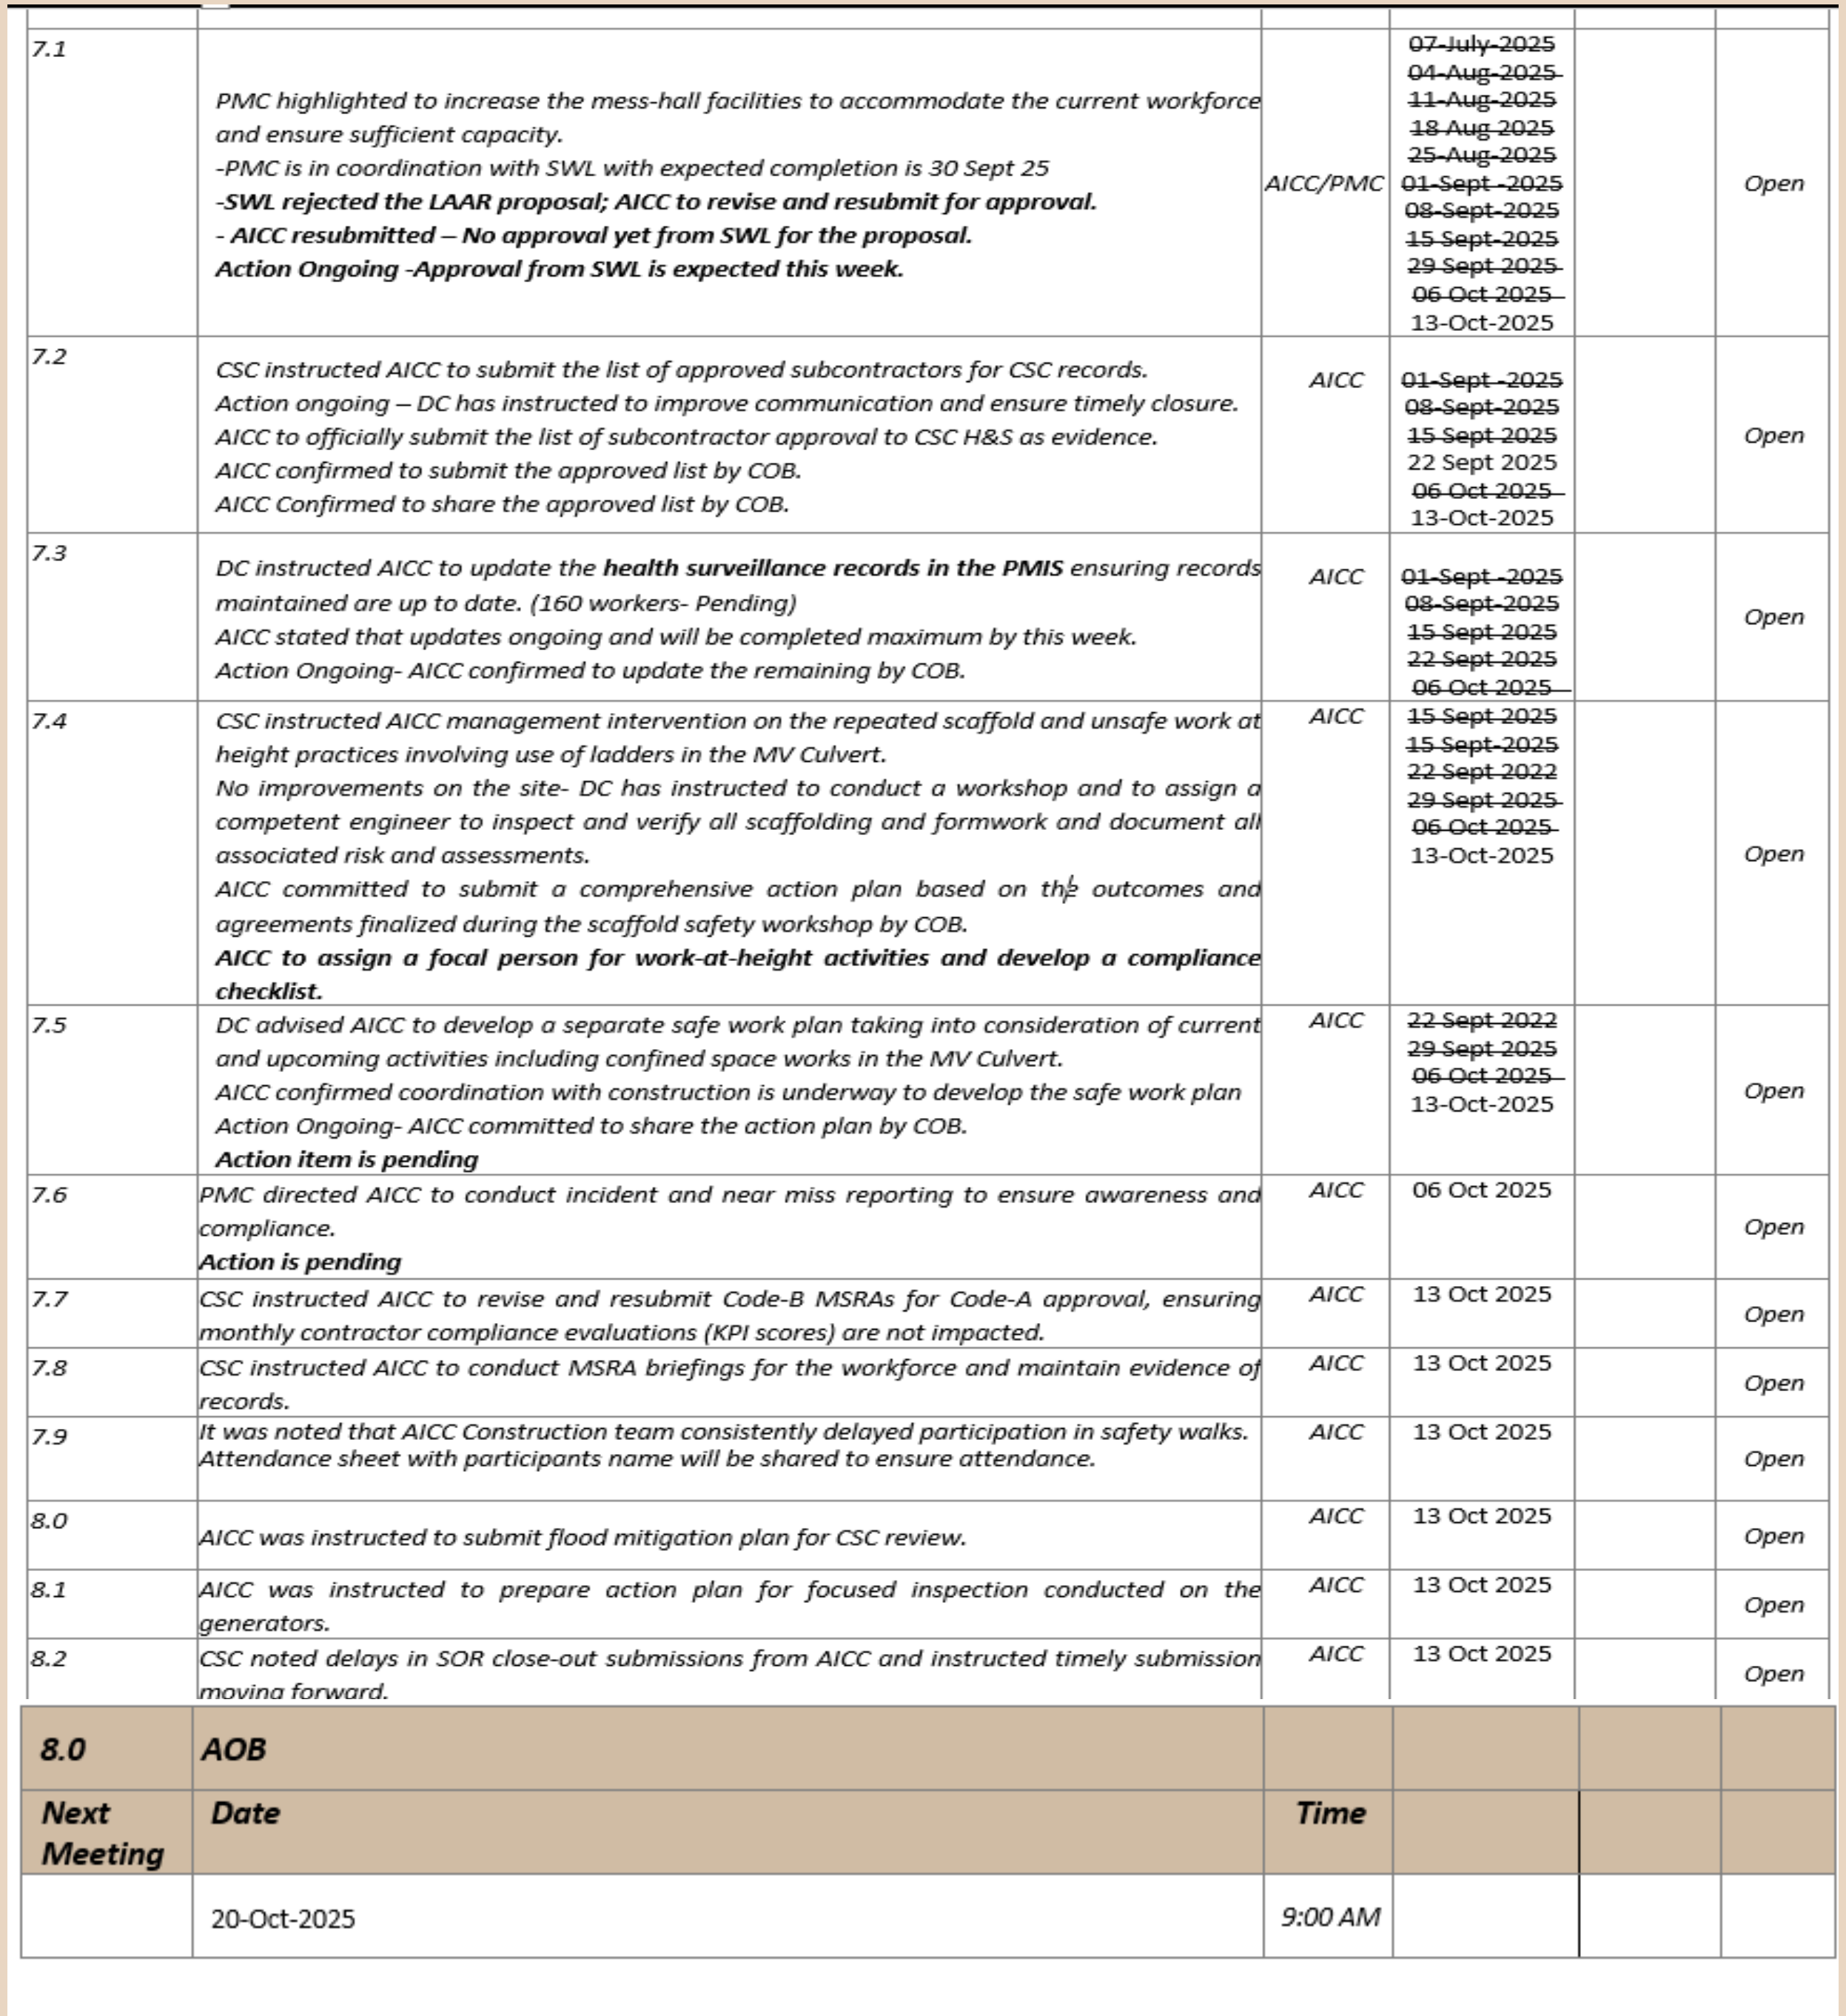

Item	Description	Action Owner	Planned/Due Date	Forecast Date	Status
7.1	*PMC highlighted to increase the mess-hall facilities to accommodate the current workforce and ensure sufficient capacity.* *-PMC is in coordination with SWL with expected completion is 30 Sept 25* ***-SWL rejected the LAAR proposal; AICC to revise and resubmit for approval.*** ***- AICC resubmitted – No approval yet from SWL for the proposal.*** ***Action Ongoing -Approval from SWL is expected this week.***	*AICC/PMC*	~~07-July-2025~~ ~~04-Aug-2025~~ ~~11-Aug-2025~~ ~~18 Aug 2025~~ ~~25-Aug-2025~~ ~~01-Sept -2025~~ ~~08-Sept-2025~~ ~~15 Sept-2025~~ ~~29 Sept 2025~~ ~~06 Oct 2025~~ 13-Oct-2025		*Open*
7.2	*CSC instructed AICC to submit the list of approved subcontractors for CSC records.* *Action ongoing – DC has instructed to improve communication and ensure timely closure.* *AICC to officially submit the list of subcontractor approval to CSC H&S as evidence.* *AICC confirmed to submit the approved list by COB.* *AICC Confirmed to share the approved list by COB.*	*AICC*	~~01-Sept -2025~~ ~~08-Sept-2025~~ ~~15 Sept 2025~~ 22 Sept 2025 ~~06 Oct 2025~~ 13-Oct-2025		*Open*
7.3	*DC instructed AICC to update the* ***health surveillance records in the PMIS*** *ensuring records maintained are up to date. (160 workers- Pending)* *AICC stated that updates ongoing and will be completed maximum by this week.* *Action Ongoing- AICC confirmed to update the remaining by COB.*	*AICC*	~~01-Sept -2025~~ ~~08-Sept-2025~~ ~~15 Sept 2025~~ ~~22 Sept 2025~~ ~~06 Oct 2025~~		*Open*
7.4	*CSC instructed AICC management intervention on the repeated scaffold and unsafe work at height practices involving use of ladders in the MV Culvert.* *No improvements on the site- DC has instructed to conduct a workshop and to assign a competent engineer to inspect and verify all scaffolding and formwork and document all associated risk and assessments.* *AICC committed to submit a comprehensive action plan based on the outcomes and agreements finalized during the scaffold safety workshop by COB.* ***AICC to assign a focal person for work-at-height activities and develop a compliance checklist.***	*AICC*	~~15 Sept 2025~~ ~~15 Sept-2025~~ ~~22 Sept 2022~~ ~~29 Sept 2025~~ ~~06 Oct 2025~~ 13-Oct-2025		*Open*
7.5	*DC advised AICC to develop a separate safe work plan taking into consideration of current and upcoming activities including confined space works in the MV Culvert.* *AICC confirmed coordination with construction is underway to develop the safe work plan* *Action Ongoing- AICC committed to share the action plan by COB.* ***Action item is pending***	*AICC*	~~22 Sept 2022~~ ~~29 Sept 2025~~ ~~06 Oct 2025~~ 13-Oct-2025		*Open*
7.6	*PMC directed AICC to conduct incident and near miss reporting to ensure awareness and compliance.* ***Action is pending***	*AICC*	06 Oct 2025		*Open*
7.7	*CSC instructed AICC to revise and resubmit Code-B MSRAs for Code-A approval, ensuring monthly contractor compliance evaluations (KPI scores) are not impacted.*	*AICC*	13 Oct 2025		*Open*
7.8	*CSC instructed AICC to conduct MSRA briefings for the workforce and maintain evidence of records.*	*AICC*	13 Oct 2025		*Open*
7.9	*It was noted that AICC Construction team consistently delayed participation in safety walks. Attendance sheet with participants name will be shared to ensure attendance.*	*AICC*	13 Oct 2025		*Open*
8.0	*AICC was instructed to submit flood mitigation plan for CSC review.*	*AICC*	13 Oct 2025		*Open*
8.1	*AICC was instructed to prepare action plan for focused inspection conducted on the generators.*	*AICC*	13 Oct 2025		*Open*
8.2	*CSC noted delays in SOR close-out submissions from AICC and instructed timely submission moving forward.*	*AICC*	13 Oct 2025		*Open*
8.0	***AOB***				
Next Meeting	***Date***	***Time***			
	20-Oct-2025	*9:00 AM*			

OH&S Weekly KPIs (Leading and Lagging Indicators)

OH&S Weekly KPIs (Leading and Lagging Indicators)				
Project Name	DG II Infra 01			
1	**MAN-HOURS**	**This Week**	**Year To Date**	**Project To Date**
1.1	Total Average Manpower	1471	899	564
1.2	Total Man-hours Worked	88230	214827	3067903
1.3	Safe Man-Hours	88230	214827	3067903
1.4	Total OH&S Personnel	27	19	7
2	**LEADING INDICATORS**	**This Week**	**Year To Date**	**Project To Date**
2.1	OH&S Leadership Site Walkthrough	1	36	70
2.2	OH&S Inductions	6 Sessions/72Attendees	1565	2137
2.3	OH&S Tool-Box Meetings/ Talks	17	460	694
2.4	OH&S Meetings	1	37	78
2.5	OH&S Trainings/ Awareness and Campaigns	9 sessions/1	337/28	469/48
2.6	Ratio of SORs closure (Open : Closed)	5/3	7/33	7/188
2.7	OH&S Internal Audits	0	1	2
2.8	OH&S External Audits	0	2	2
2.9	OH&S Emergency Drills	0	2	6
2.10	OH&S Rewards and Recognitions	0	4	14
3	**LAGGING INDICATORS**	**This Week**	**Year To Date**	**Project To Date**
3.1	Work-Related Fatality	0	0	0
3.2	Lost Time Incident (LTI)	0	0	0
3.3	Total Recordable Incident Rate (TRIR)	0	0	0
3.4	Restricted Workday Cases (RWDC)	0	0	0
3.5	First Aid Case (FAC)	0	1	1
3.6	Medical Treatment Case (MTC)	0	0	0
3.7	Near Miss	1	8	11
3.8	Occupational Illness	0	0	0
3.9	Dangerous Occurrence	0	0	0
3.10	Fire Incident	0	0	0
3.11	Motor Vehicle Accident (MVA)	0	1	1
3.12	Property Damage	0	6	10
2.13	Environmental Incident	0	0	3
3.14	Non-Work-Related Fatality	0	0	0
3.15	Non-Work-Related Injury and Ill health	0	4	4

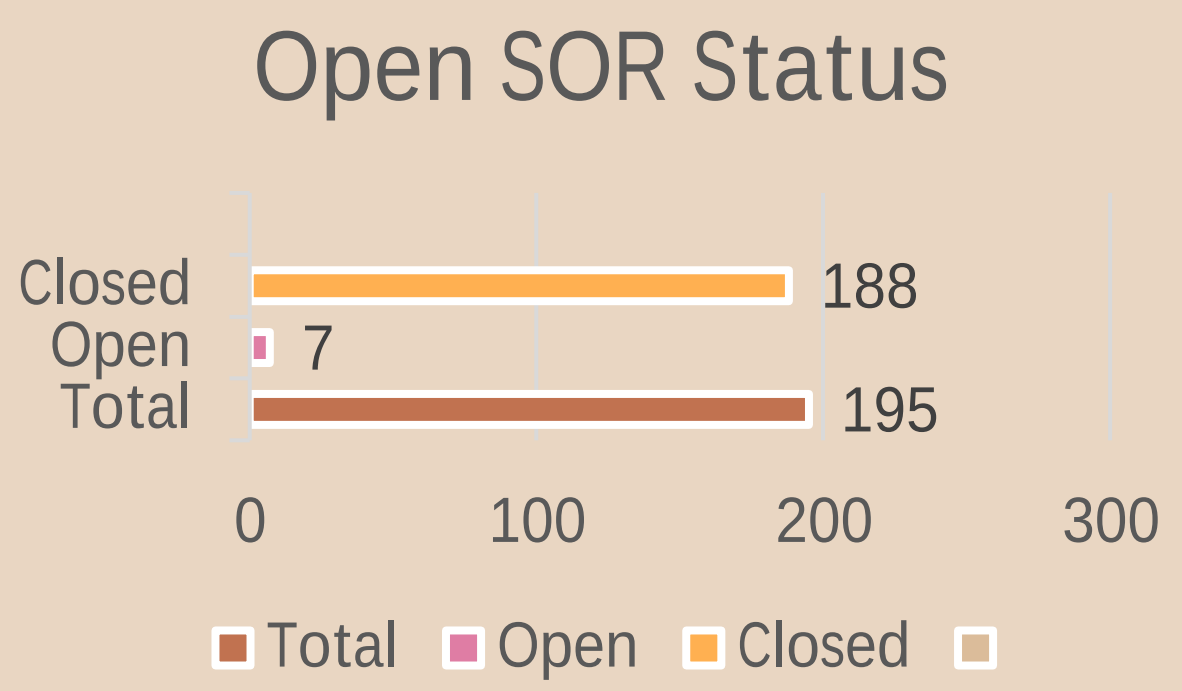
Open SOR Status

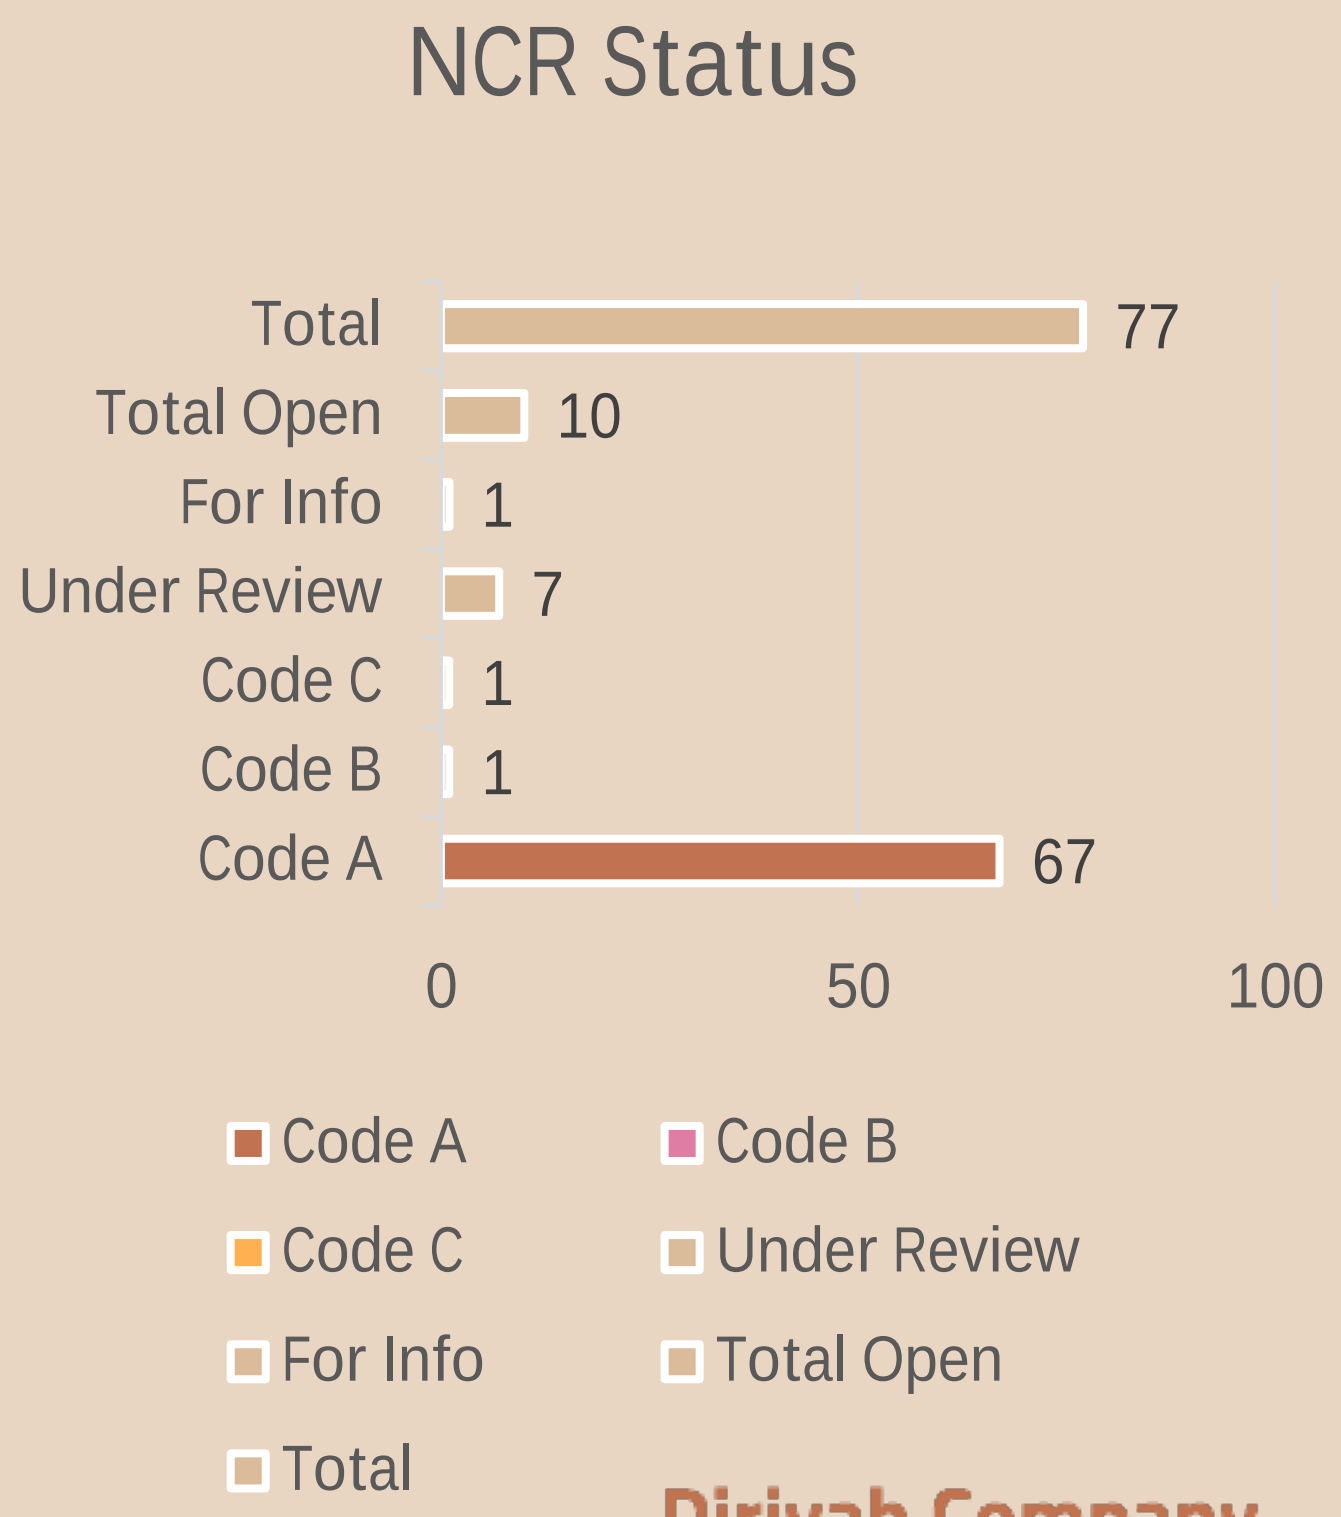
NCR Status

Diriyah Company

Near Misses (Internal)

1

Description- A worker was observed working on top of a mobile scaffold while wearing a body harness. However, the safety hook (lanyard) was not connected to any anchorage point. This means that although the worker was equipped with fall protection equipment, it was not properly used, leaving him fully exposed to the risk of falling at SEG 53

Status-Closed

2

العيوني
AL-AYUNI
11/10/2025, 9:44 AM
Diriyah
AICC

Description- A worker was observed working on top of a mobile scaffold while wearing a body harness. However, the safety hook (lanyard) was not connected to any anchorage point. This means that although the worker was equipped with fall protection equipment, it was not properly used, leaving him fully exposed to the risk of falling at SEG 53

Status-Closed

3



Description- In Grand mosque, concrete breaking activity was ongoing .an air compressor was found parked dangerously close to the edge of the excavation. Workers are working insidethe excavation. The position of the equipment posed a serious risk of collapse, which could have resulted in equipment damage, potential injury, or a fatal incident.

Status-Closed

4

Description- On October 13, 2025 around 7:45 AM workers were on a scaffold without provision of edge protection, safe working platform, safe access and lifeline for top slab shutter work. There is a high probability that they can fell down and this can lead to an unfavorable incident

Status-Closed

5



Description- During night lifting operations at MVC SEG 55 , shuttering materials were being loaded using a crane. The crane's swing radius came in close proximity to a nearby light pole, posing a potential collision hazard.

No damage or injury occurred; however, the incident highlights the need for proper lifting area assessment, pre-lift planning, and maintaining a safe clearance from fixed structures.

Status-Closed

6

Description- Worker observed working outside the guardrail, exposing himself to a potential fall hazard. Although proper edge protection is installed, the worker bypassed the guardrail — an unsafe act that could have led to a serious fall incident sub con name (Technical proof) at SEG 55

Status-Closed

Near Misses & Observation(Internal)

Weekly Power App Observation & Near Miss (Target /Achievement) Week No-41 / Oct 11th-2025 to Oct 17th 2025

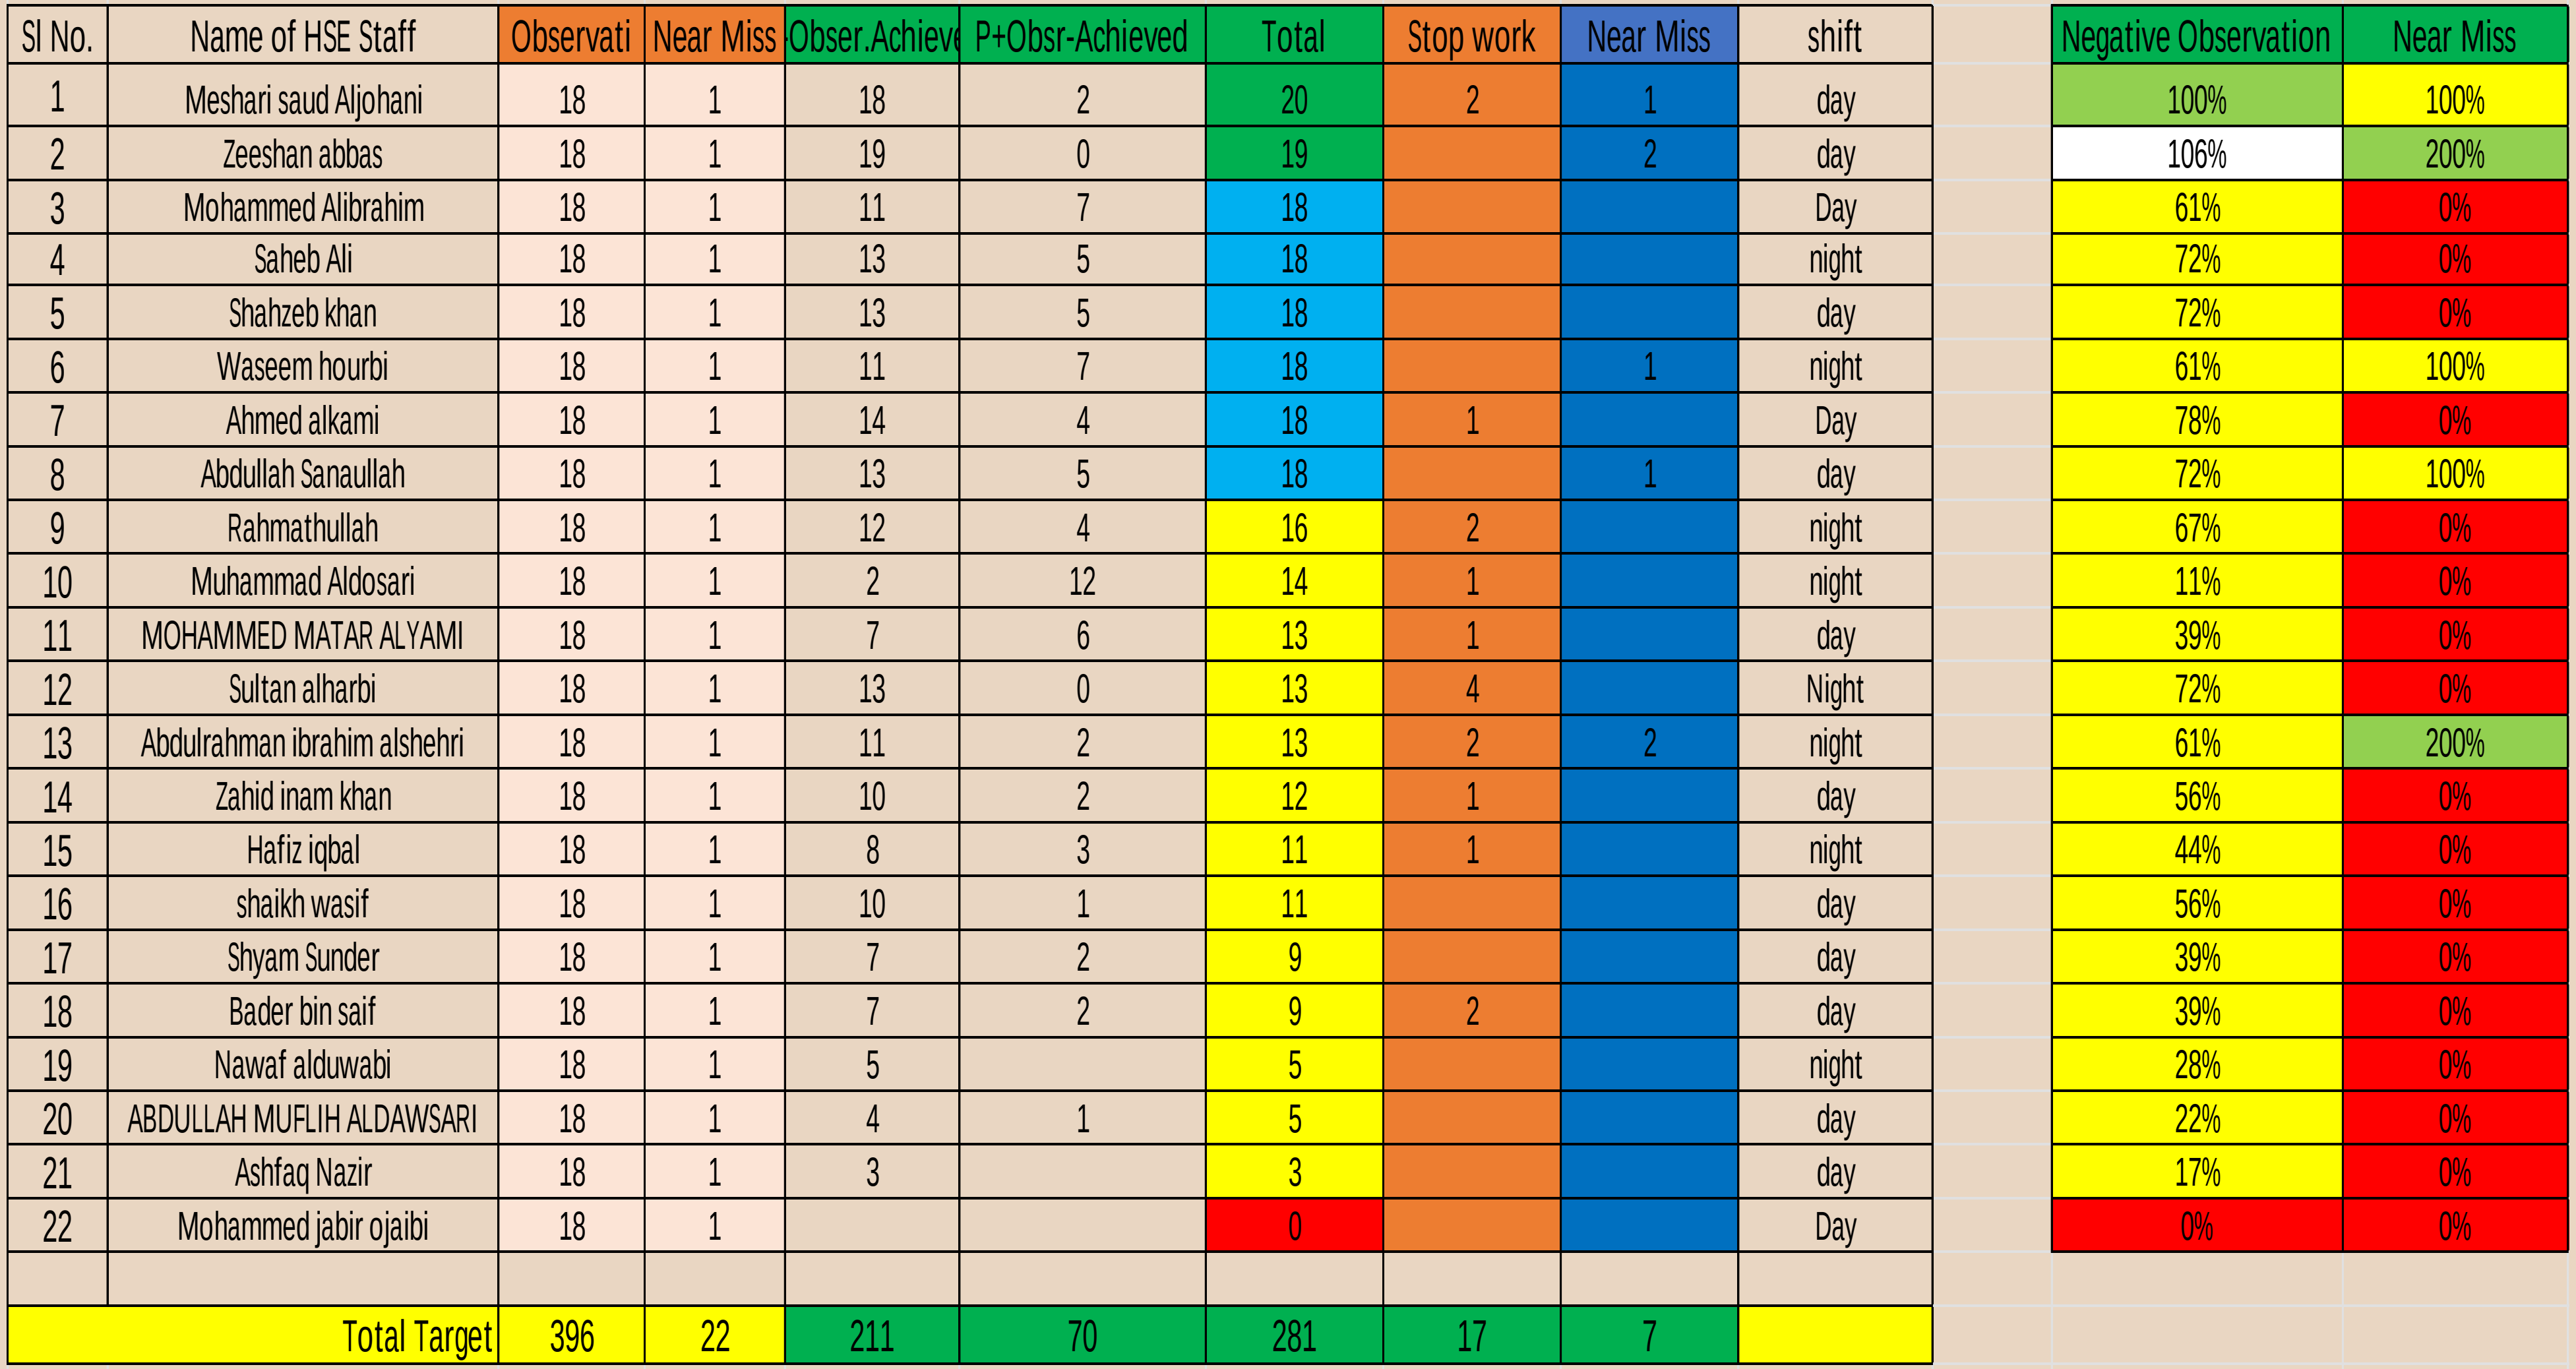

Sl No.	Name of HSE Staff	Observati	Near Miss	Obser.Achieve	P+Obsr-Achieved	Total	Stop work	Near Miss	shift	Negative Observation	Near Miss
1	Meshari saud Aljohani	18	1	18	2	20	2	1	day	100%	100%
2	Zeeshan abbas	18	1	19	0	19		2	day	106%	200%
3	Mohammed Alibrahim	18	1	11	7	18			Day	61%	0%
4	Saheb Ali	18	1	13	5	18			night	72%	0%
5	Shahzeb khan	18	1	13	5	18			day	72%	0%
6	Waseem hourbi	18	1	11	7	18		1	night	61%	100%
7	Ahmed alkami	18	1	14	4	18	1		Day	78%	0%
8	Abdullah Sanaullah	18	1	13	5	18		1	day	72%	100%
9	Rahmathullah	18	1	12	4	16	2		night	67%	0%
10	Muhammad Aldosari	18	1	2	12	14	1		night	11%	0%
11	MOHAMMED MATAR ALYAMI	18	1	7	6	13	1		day	39%	0%
12	Sultan alharbi	18	1	13	0	13	4		Night	72%	0%
13	Abdulrahman ibrahim alshehri	18	1	11	2	13	2	2	night	61%	200%
14	Zahid inam khan	18	1	10	2	12	1		day	56%	0%
15	Hafiz iqbal	18	1	8	3	11	1		night	44%	0%
16	shaikh wasif	18	1	10	1	11			day	56%	0%
17	Shyam Sunder	18	1	7	2	9			day	39%	0%
18	Bader bin saif	18	1	7	2	9	2		day	39%	0%
19	Nawaf alduwabi	18	1	5		5			night	28%	0%
20	ABDULLAH MUFLIH ALDAWSARI	18	1	4	1	5			day	22%	0%
21	Ashfaq Nazir	18	1	3		3			day	17%	0%
22	Mohammed jabir ojaibi	18	1			0			Day	0%	0%
Total Target		396	22	211	70	281	17	7			

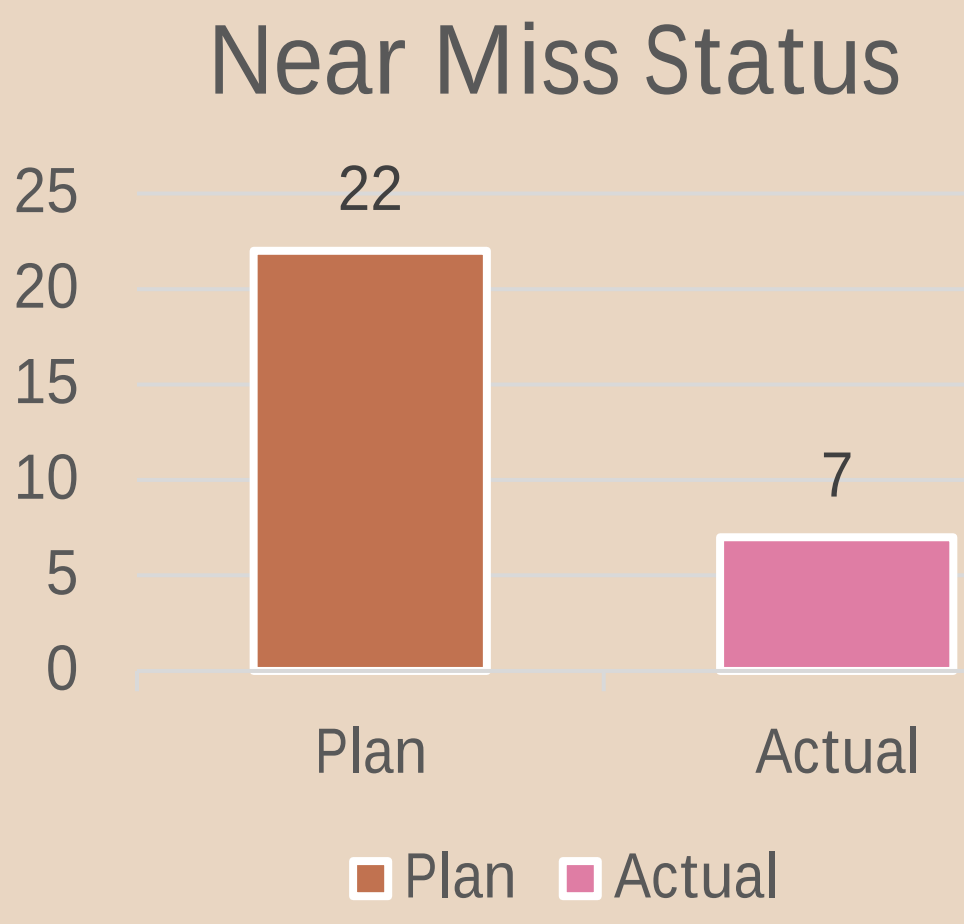

OHS Achievements / Highlights / Activities

Network: 12-Oct-2025 at 7:22:33 AM
Local: 12-Oct-2025 at 7:22:33 AM
Remark: SH
FIRE POINT
12 Oct 2025 at 7:37:35 AM
Ad Dir'iyah
AL-AYUNI

A fire extinguisher safety and operational refresher training session was conducted on site to raise workers' awareness and competence in handling fire emergencies effectively.

AL-AYUNI
Jacobs
Riyadh
Remark: DG II
Network: 13 Oct 2025 8:09:34 am GMT+03:00
Google

Weekly Safety Walkthrough has been conducted

Major OHS Concern's

1. Heat stress prevention program to be implemented.
2. Shotcrete MV Culvert excavation.
3. MV Culvert Geotech Assessment

OHS Achievements / Highlights / Activities

العيوني AL-AYUNI
Network: 16 Oct 2025 at 12:39:22 pm GMT+3
Local: 16 Oct 2025 at 12:39:22 pm GMT+3
N 24° 43' 8.158", E 46° 35' 20.369"
85° E
Riyadh Region 12573 ,الدرعية
Remark: DIRIYAH - DGCL - Riyadh
W.Rashed
Maps
TECHNO PROOF
Network: 16 Oct 2025 at 12:36:20 pm GMT+3
Local: 16 Oct 2025 at 12:36:20 pm GMT+3
N 24° 43' 8.286", E 46° 35' 21.643"
305° NW
Riyadh Region 12573 ,الدرعية
Remark: DIRIYAH - DGCL - Riyadh
W.Rashed
Network: 16 Oct 2025 at 12:32:17 pm GMT+3
Local: 16 Oct 2025 at 12:32:17 pm GMT+3
N 24° 43' 8.361", E 46° 35' 20.714"
86° E
Riyadh Region 12573 ,الدرعية
Remark: DIRIYAH - DGCL - Riyadh
W.Rashed

A headcount of all Contractor and Subcontractor personnel was carried out to verify the actual manpower currently mobilized at the project site

Major OHS Concern's

1. Heat stress prevention program to be implemented.
2. Shotcrete MV Culvert excavation.
3. MV Culvert Geotech Assessment

NCR’s & SOR Status

Critical Open SORs, SVR / NCRs

NCRs

#	NCR No.	Date of Issuance	CAPA due date	Variance (days)	Subject	Status
1	42	5th July 2025	15th July 2025		Non-Compliance of Excavations	Revise & Resubmit
2	60	31st August 2025	8th September 2025		Scaffolding Safety Non-Compliance – (Instability, Improper tagging, and Unauthorized Material loading)	Under Review
3	62	3rd September 2025	2nd October 2025		Unsafe Condition of Excavation Wall	Under Review
4	63	4th September 2025	2nd October 2025		Unsafe Condition of Excavation Wall - (Road 03)	Under Review
5	69	13th September 2025	20th September 2025		Unsafe working condition and using sub-standard	Under Review
6	73	27th September 2025	7th October 2025		Repeated and Unacceptable failure to provide pedestrian protection for workers and project personnel	Under Review
7	75	8th October 2025	16th October 2025		Unsafe excavation condition at Grand Mosque Sewer Diversion Zone	Under Review
8	76	11th October 2025	19th October 2025		Inadequate Personnel Accountability and Site Entry/Exit Control	Open
9	77	12th October 2025	19th October 2025		Repeated Safety Non-Compliance – Unsafe Excavation condition, Equipment Deficiencies and Permit-	Under Review

Critical Open SORs, SVR / NCRs

NCRs

#	NCR No.	Date of Issuance	CAPA due date	Variance (days)	Subject	Status

SORs

Last week SOR's Observations	CLOSED	OPEN	On Progress	Overdue
49	10	20	19	0

TOTAL SOR's (PTD)	CLOSED	OPEN	On Progress	Overdue
195	188	5	2	2

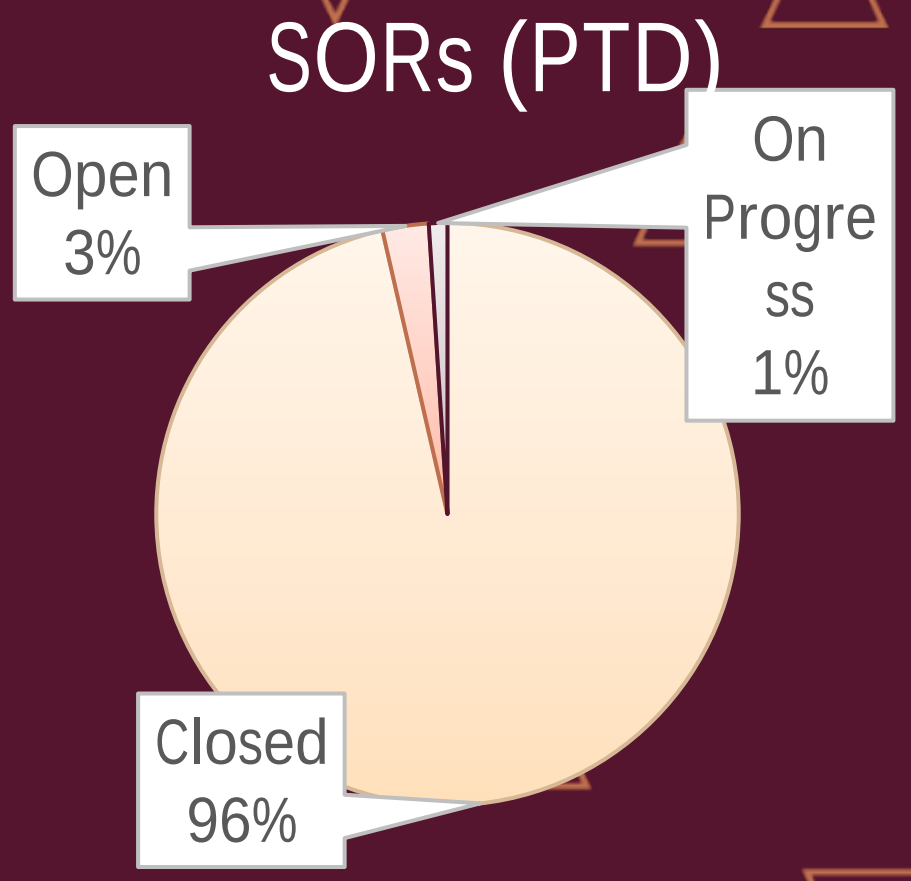

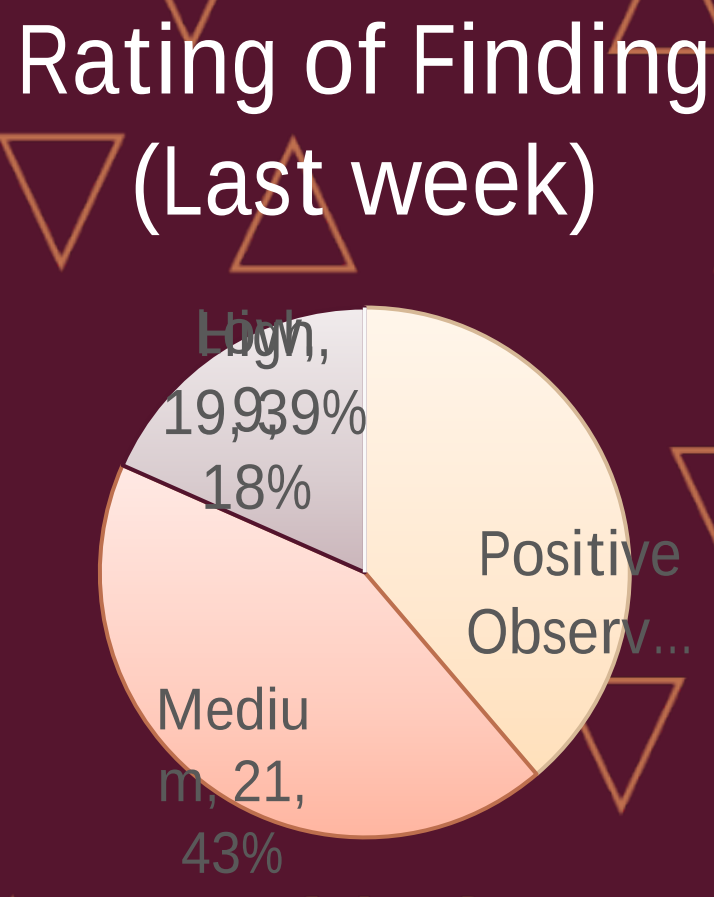

Diriyah Company

OH&S Weekly KPIs

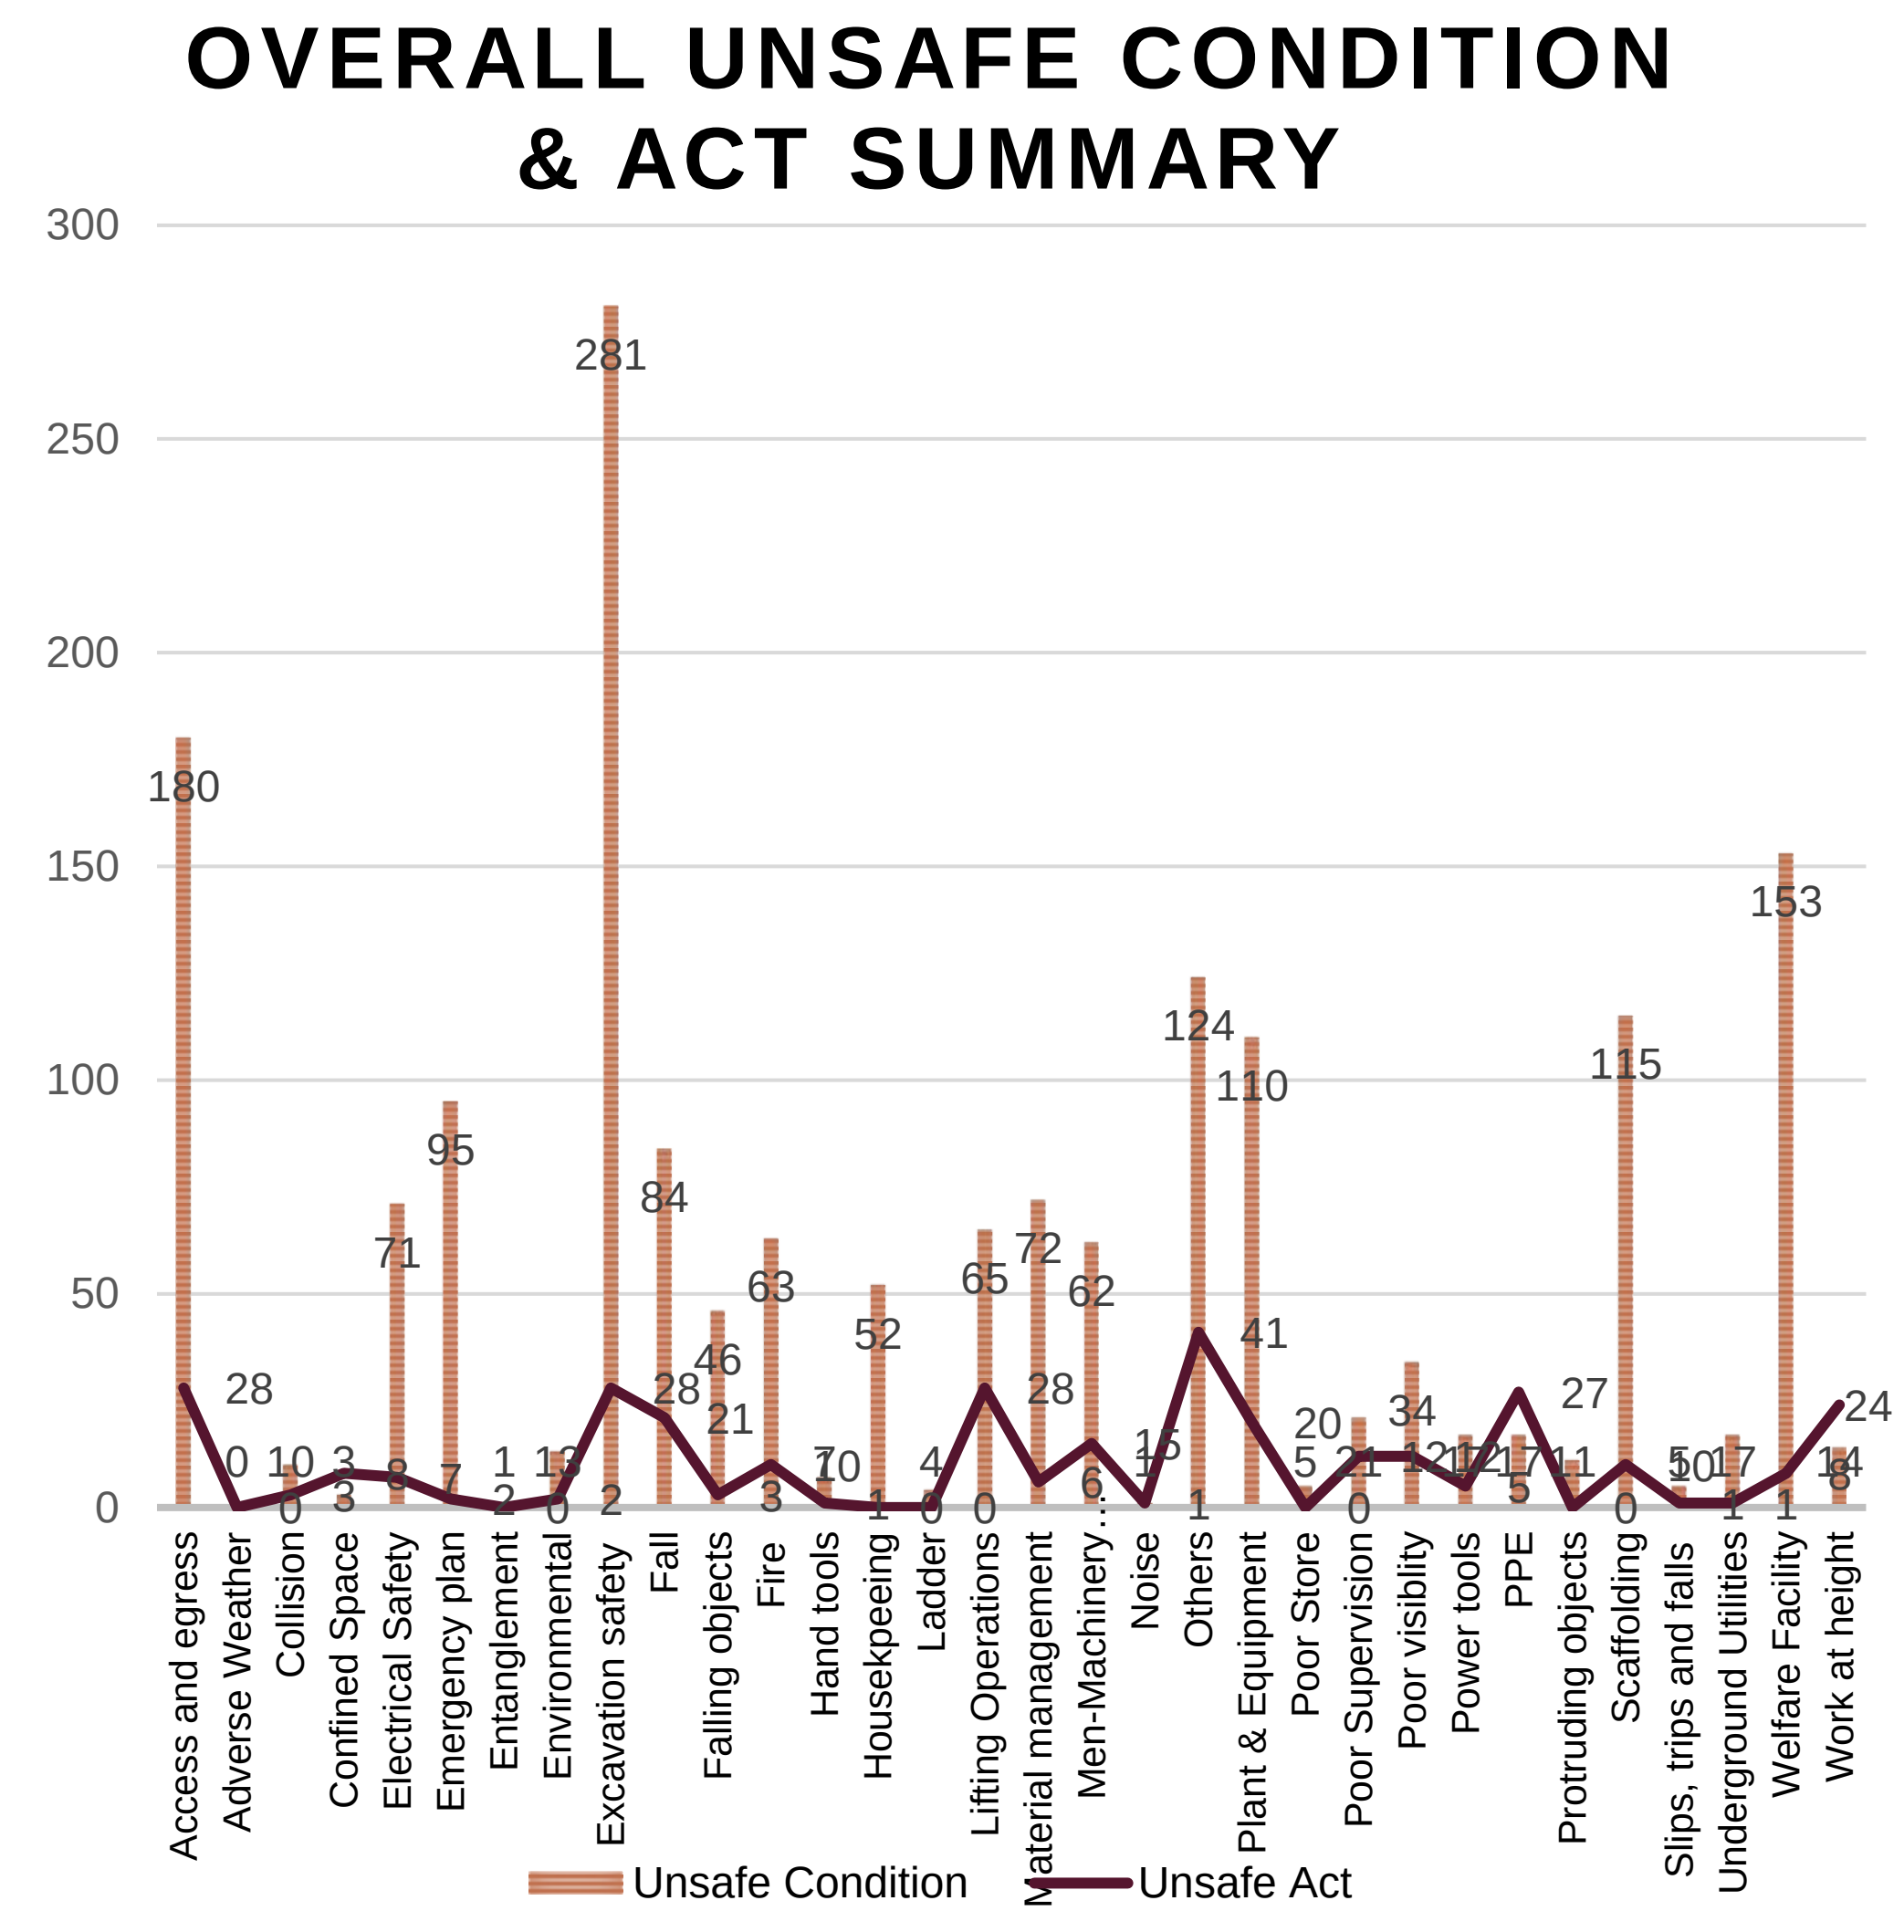

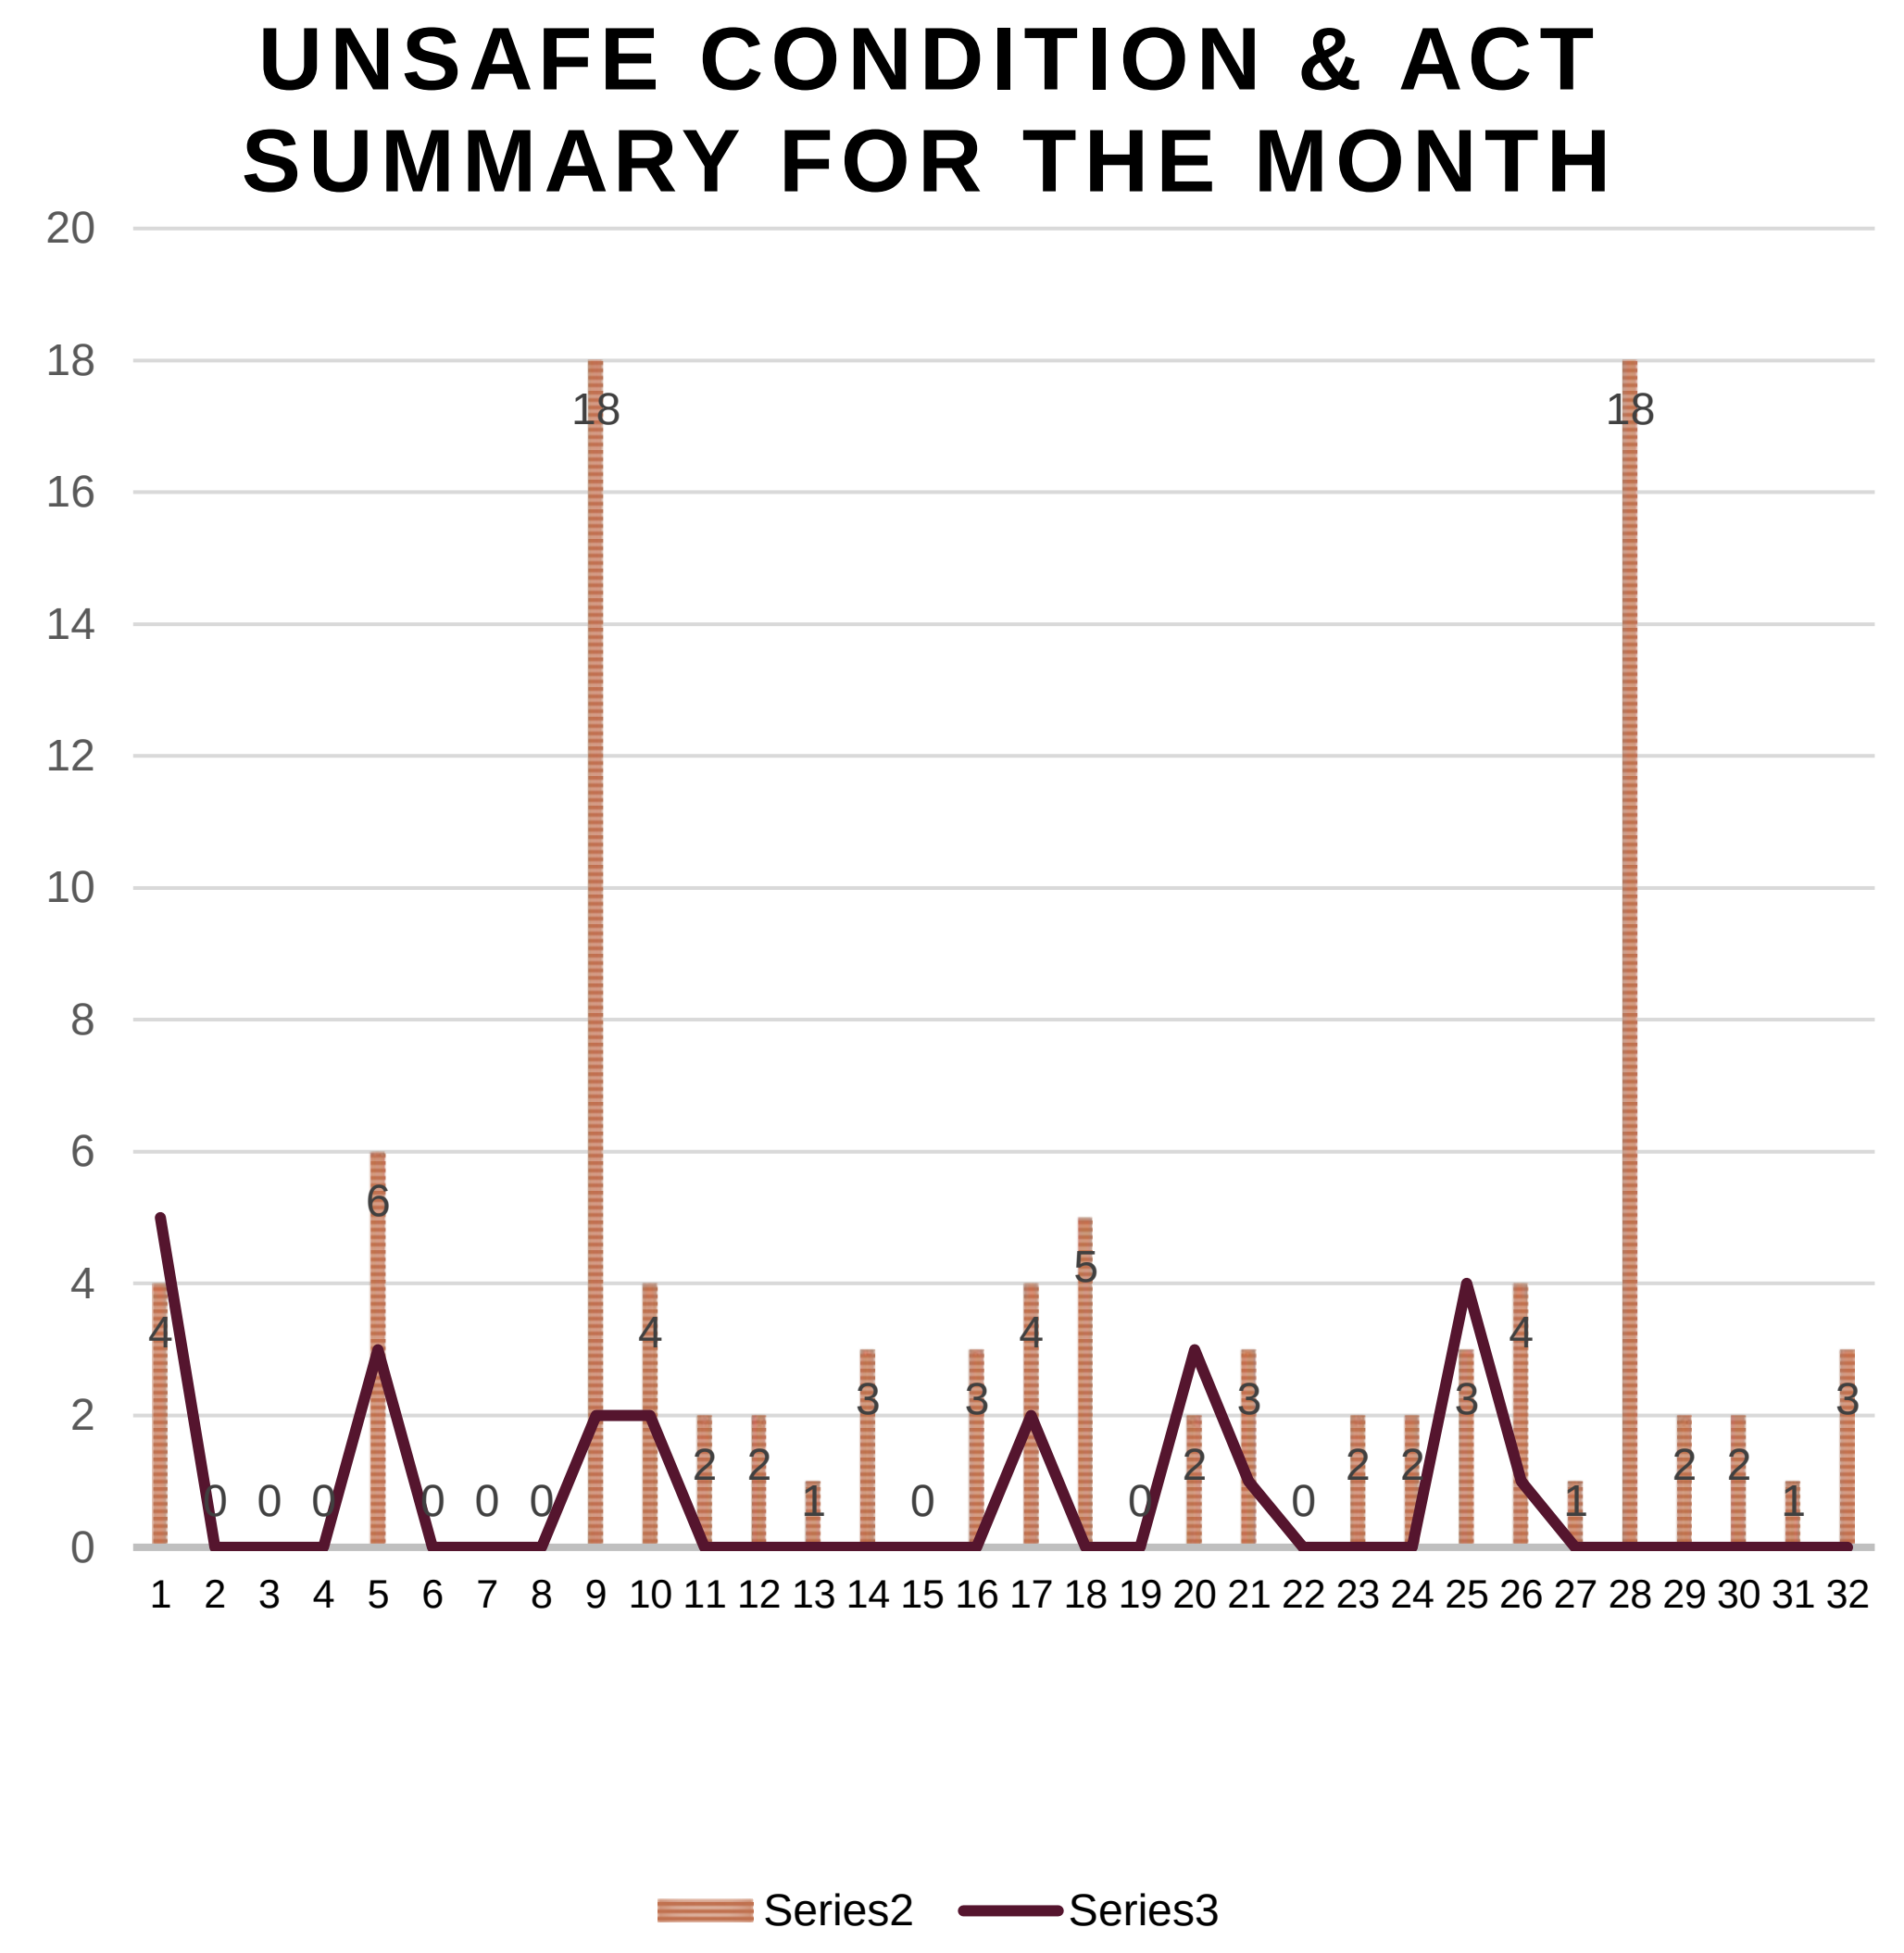

Others`
No defined parking
no LAAR boundary
signages
Lack of Training & Induction
non availability of MSRA
Poor Barrication
Fence boundary missing
Poor Stockpile management
Improper coordination
works without NTS
Competency Cards missing
Unsafe temporary supports
No site layout
Lack of Permits
Chemical handling
MSDS
barriers close to edge
Poor traffic Management
PTW

Incidents & Significant Near Misses

At 10:45 PM A worker was observed transporting a leaking jerry can of petrol through the MV-Culvert, a designated restricted and confined route. A strong odor of fuel was present, and a visible trail of drips was noted along the path. While no ignition source was identified and no injuries occurred, the situation presented a credible risk of fire, explosion, and inhalation exposure due to the confined nature of the area and the presence of flammable vapors.

▶

MV Culvert-Segment- 27

12:20:00 PM

12/10/2025

EMGT Statistics

EMGT Statistics	
Description	**Current Week**
Major Incidents	0

- NA

Major Incidents (S4 & S5)

Location Name/Project 00:00 DD/MM/YYYY

Brief

- None

Action Taken

- None

Pictures

OH&S Submittals Status (Plans, Procedures, etc.)

S. No	Action Item	Due Date	Action by	Status	Forecast /Completed Date	Comments
1						
2						
3						
4						
5						
6						

Next Week Look Ahead Major Construction Activities

Activity / Task

1. Excavation Pipe laying, testing & backfilling of Storm Water/Potable, Wastewater /irrigation Network R0 (Media, Southern, 1d Northern West, 1e Northern East Boulevard Northwest & Boulevard Northeast) and Granules Material backfilling & Compacting work at MV Culvert
2. Lifting in Media 1a, Northern west Ie-Southern, Road 3, Road 5, Road 1, media 1, Road-06, Road 3-02, Rd 07-13 Rd 07-10
3. Cast In-Situ Concretes works for MVC, under pass & Boulevard
4. Diversion and Excavation of Existing Potable Water Line (General Works) Near Grand Mosque/SAMOKA (Pump Station 2)
5. Confined space (Working inside manhole)
6. Access Scaffolding Cup-lock & Shore Brace Frame System
7. Steel & Concrete works and Bitumen Coating and Waterproofing in MV Culvert & (MVC Roof work)
8. Erection, Modification & Dismantling of Scaffolding in MVC
9. Excavation & Backfilling in WWPS (Wastewater Pump Station)
10. Earth work in Gateway

Weekly OHS Activities

Project	OHS Walkthrough	OHS Meeting	Individual Site OHS Inspections	Award & Celebrations Campaigns /Training	Focused Inspection
DG2 - INFRA 01	1	1	1	0/09	0

DG-II Infra 01

No.	Activity / Task	Project / Location	MSRA	Remark
1	TPM	GM	Submitted	
2	Civil works	MV Culvert	Submitted	
3	Earth work gateway	Gateway	Submitted	
4	Welfare Land	New LAAR	Submitted	
5	MEP Works	GM	Submitted	
6	Road Works	Gateway	Submitted	

Thank you

OH&S Attendance List

Location/Project Name:	Infra Package_01
Topic Discussed	OHS Weekly Meeting/ Two week look ahead Plan
Company Name:	DC/PMC/ CSC/ AICC

Sr. No	Employee Name	Trade	Company	Date	Signature
1	Magid Saleh	ABM	AECom	20-X-25	
2	Metaeb Alharbi	OHS	DC	"	
3	Walid Rashed	OHS	AICC	"	
4	Ali Nabil	OHS	Jacobs	"	
5.	Adel Alharbi	S.OHS.M	Jacobs	"	
6	Muneer Ali	LO	JACOBS	"	
7	Susheel Kurup	OHS	AECOM	"	
8	Hamzah Alghamdi	OHS	AECom	"	
9	Asma Othman	OHS	DC	"	
10	IMRAN S KHAN	"	AECOM	"	
11	RAJEH	"	DC	"	
12	M-Musa	"	MCP.M AICC	"	
13	ROMANTO	HSE	JACOBS	"	
14	Burabi Muhamma	OHS	=	=	
